


FIRST DAY

Project Status and Roadmap Briefing

A presentation-ready account of what we built together, how progress is estimated, and what remains before launch.

REPORT 04 | AS OF 05 OCTOBER 2026, 08:25 (+06:00)

Based on the Helpyard.store New Implementation Plan v2.0

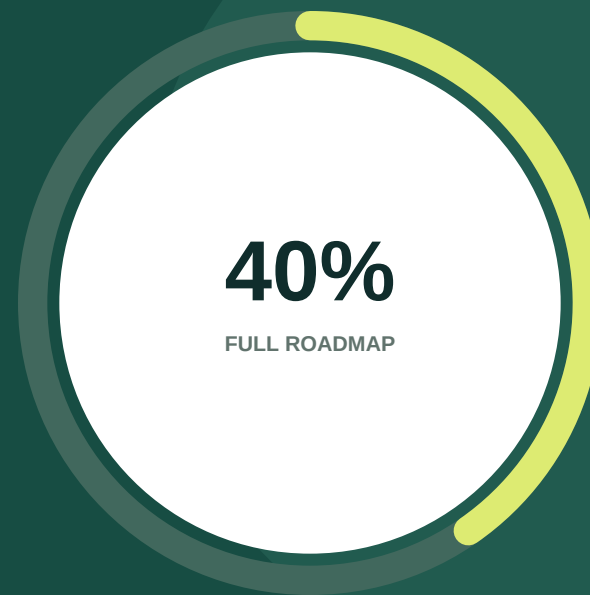

46.5%

PRE-PRODUCTION PHASES 0-12

+3 pp

SINCE REPORT 03

EXECUTIVE READOUT

Core storefront and commerce flows now have real local database evidence for stock contention and payment-review cases, and administrators can inspect orders in a new read-only console. **This is progress, not launch approval:** Gate 0, hosted CI, payment sandbox, and production acceptance remain open.

The build journey, step by step

Use this sequence as the narrative for your presentation: problem alignment → useful flows → operations → evidence → next gate.

- 01

Read the v2 roadmap
We grounded work in the 15-phase plan and identified the next unmet milestone rather than adding features at random.
- 02

Deliver course learning
Paid orders create access; customers can open lessons and record progress.
- 03

Build admin operations
Added trusted CLI admin provisioning, private file upload/revocation, and protected downloads.
- 04

Manage catalog safely
Added audited category/product management, inventory controls, and hidden-category safeguards.
- 05

Prepare and prove Gate 0
Created decision/wireframe drafts and MySQL CI integration coverage; ran all 14 migrations and seeders locally.
- 06

Stabilize checkout & review
Tested parallel stock contention and payment risk/late/rejection paths; added a read-only admin order-review console.

A SIMPLE PRESENTATION FLOW

- 1 START**
We followed the approved roadmap order.
- 2 SHOW**
Demonstrate storefront, customer access and admin workflows.
- 3 MEASURE**
Explain the estimate and what evidence changed it.
- 4 BE HONEST**
Name open approvals, sandbox and deployment gates.
- 5 ASK**
Request decisions and access needed for the next milestone.

SAMPLE 30-SECOND SUMMARY


We built the core storefront and operations flows, and local MariaDB now verifies stock contention and payment review. Progress is about 40%; owner sign-off, hosted CI and the payment sandbox remain.

How complete is the project?

Evidence-weighted phase scores from v2.0. Scores are directional estimates, not task counts, effort spent, or a release-readiness score.

605 / 1500 phase-points = 40.3% → 40% FULL ROADMAP

605 / 1300 phase-points = 46.5% → 47% through pre-production phases 0-12

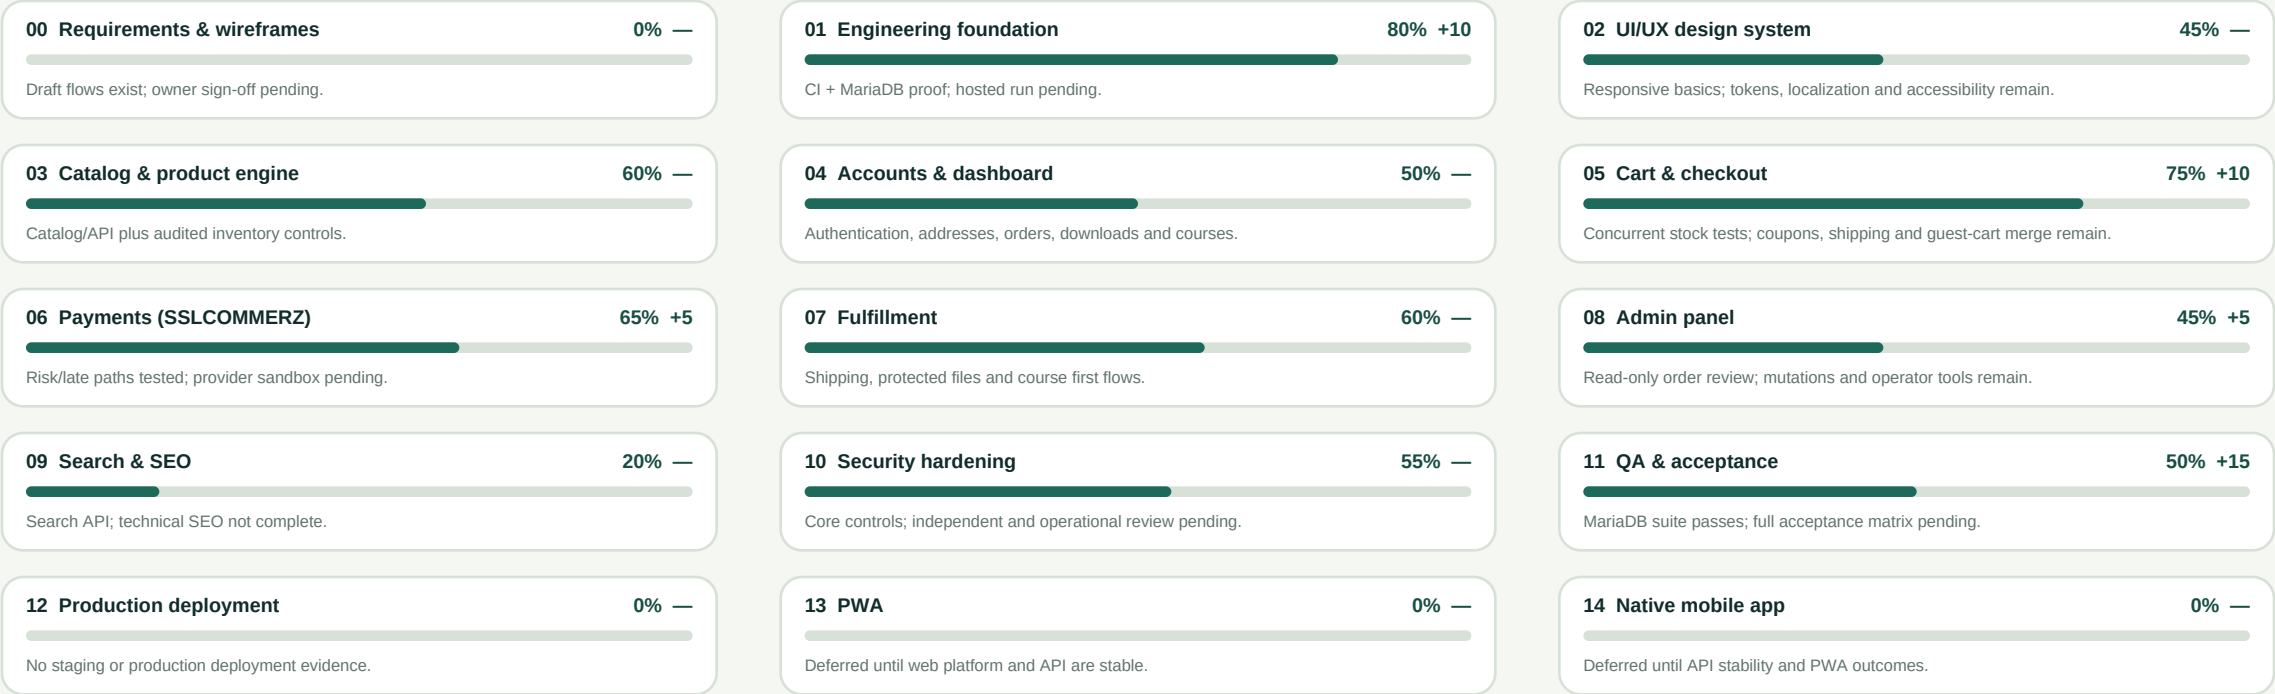

IMPORTANT GATE CHECK

The estimate exceeds the plan's approximate M0 percentage target, but **Gate 0 remains open**: owner approvals and hosted MySQL 8.4 CI are pending. Percentages never override acceptance criteria.

What happens next

Keep the order risk-first. Move to new feature scope only after the active release gate is satisfied.

NOW	Close Gate 0 Approve product and operating decisions; approve the sitemap/wireframes; get clean migration/integration evidence in hosted CI.	GATE OPEN
NEXT	Complete S1 stabilization Run MySQL 8.4 CI, execute the SSLCOMMERZ sandbox matrix, finish payment-review procedures and fix defects.	ACTIVE
THEN	Complete operations Add approved order/payment-review actions, course authoring, customer/content/support tools and operator workflows.	PLANNED
LATER	Commerce & quality Design system, localization, shipping/coupons, customer lifecycle, licensing, SEO/accessibility, hardening and release QA.	PLANNED
RELEASE	Stage, accept, launch Prove TLS/secrets, scheduler, monitoring, backup restore, rollback and production smoke checks.	NOT STARTED

NEXT DECISIONS / DEPENDENCIES

Product/business owners: sign Gate 0 decisions and design. Technical owner: run/observe hosted CI and approve the payment sandbox test plan. Business/finance owner: define manual reconciliation, refunds and late-payment handling before any admin mutation workflow is built.

The remaining work, grouped for clarity

This is the full forward-looking checklist represented in the v2 roadmap and current implementation notes; items are not yet accepted as complete.

01 BUSINESS & DESIGN

- Approve product scope, prices, delivery, roles, refunds and licensing policy.
- Approve sitemap, desktop/mobile flows and acceptance criteria.
- Define localization, accessibility and design-system direction.

02 FOUNDATION & RELEASE

- Hosted MySQL 8.4 CI, migrations and repeatability proof.
- Staging/production, TLS, secrets, scheduler, monitoring and rollback runbook.
- Backup/restore drill, load checks and production smoke acceptance.

03 CUSTOMER LIFECYCLE

- Email verification and password recovery.
- Wishlist, complete account dashboard and observable notifications.
- Support/customer operations tooling and policies.

04 COMMERCE & PAYMENT

- SSLCOMMERZ sandbox success, cancel, fail, repeat, late and risk scenarios.
- Approved reconciliation/refund workflow and admin payment-review resolution.
- Coupons, shipping zones/rates and guest-cart merge.

05 DELIVERY & CONTENT

- Signed/expiring downloads and usage limits; revocation policy.
- Course authoring/media, product images/content and software/site licensing.
- Delivery notifications with observable failure handling.

06 QUALITY & GROWTH

- SEO metadata, canonicals, sitemap, robots, structured data and internal links.
- Independent security review; accessibility, browser and performance QA.
- PWA/API v1 then native app only after web platform stability.

PRESENTATION CLOSE:

Ask for Gate 0 sign-off, hosted CI ownership, sandbox access, and the business decision-maker for payment reconciliation/refunds. These unlock the next safe build steps.
